



Remote Sensing Applications Division (RSAD)

CDR Program Office

Weekly Report for May 30, 2014
Ed Kearns, Acting Chief




CDR Program Office

NOAA NEXRAD Reanalysis


Weekly Report – May 29, 2014

NNR – NOAA NEXRAD Reanalysis

- Obtain 2010 2008 2004 QPE data from NSSL
- Present Project Overview to Stewardship Council
- Process 2007 (Severe Weather and Hydro)
- Obtain 2001 data from NCDC archive
- Develop Bias Adjustment Plan
- Transfer GCHN-Daily, and HADS data to NSSL
- Present at Weather Radar Symposium
- Process 2006 2007 2009 20011 data

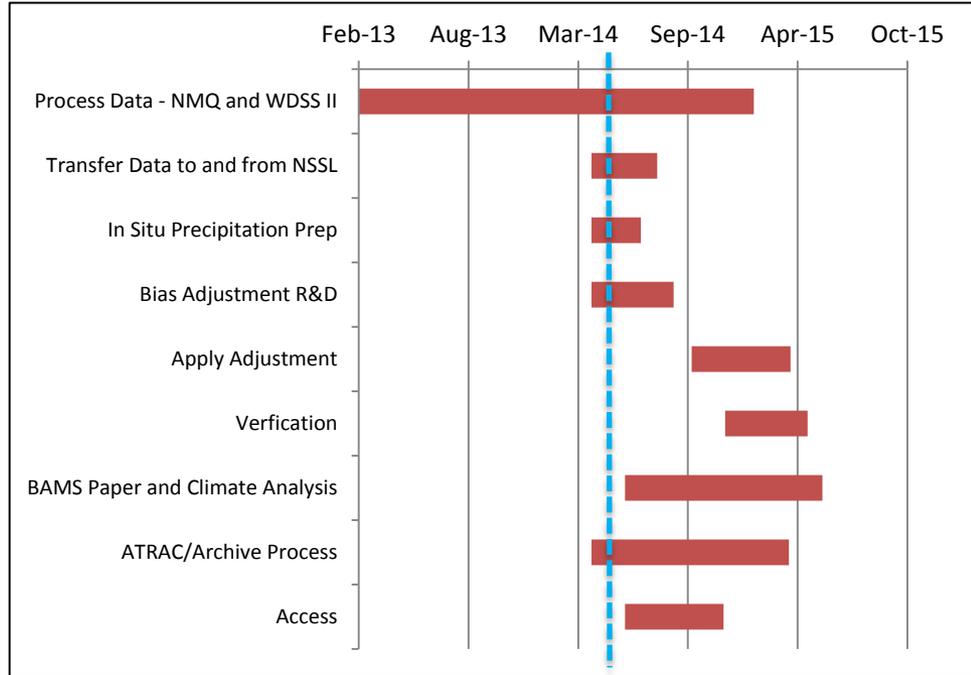

Risk Matrix

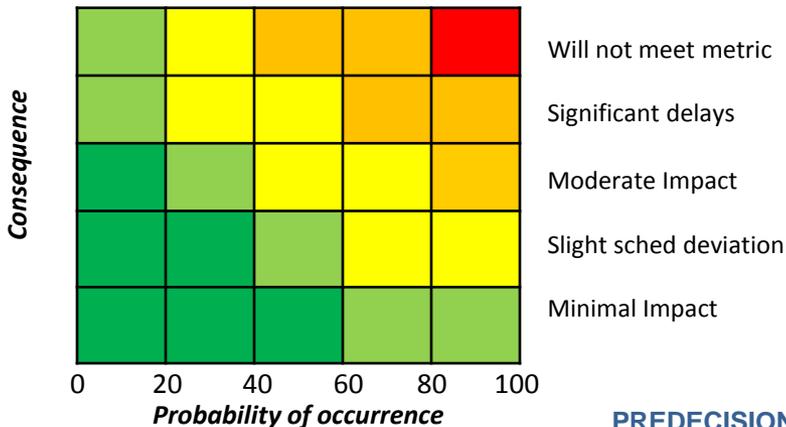

Risk and Mitigation

No Risk at this time



CDR Program Office

NPP/JPSS Climate Raw Data Records (C-RDRs) Project

Weekly Report – May 30, 2014

VIIRS

①

- Completed code for C-RDR.

②


System Infrastructure

- Integrating with the VIIRS C-RDR.
- Determining best mechanism to release C-RDR software.**
- Responding to C-RDR interest at the STAR JPSS science meeting.**
- C-RDR web page is up and running.
- Working to generate a current supporting data file.
- VIIRS C-RDRs are operational and accessible via HAS.
- Collection level metadata available on Climate.gov and DOI.org.
- Evaluating JPSS support data Change Requests and their effects.
- C-RDR is first product moving to three tier environment .
- Initial verification of SDR from C-RDR compared successfully.
- VIIRS Product Specification is ITAR approved.
- Will deliver initial version with ADL 3.1.

C-RDR Project	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY
Milestones							▲		▲▲								
Finalize Code						■											
TEST						■	■	■	■								
Dry Runs						■	■	■	■								
SAT									■								
OPERATIONS										■							
Prepare OPS										■							
Operations										■	■	■	■	■	■	■	■
Analyze Monitor																■	■
CR: Support Data																	■

R2O PHASE: ANALYSIS DESIGN DEVELOPMENT INTEGRATION TEST OPERATIONAL

Risk Matrix

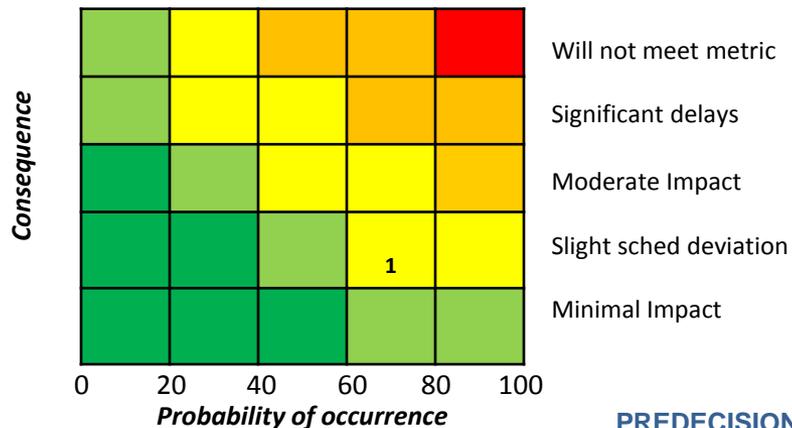

Risk and Mitigation

Forward processing of C-RDRs is ongoing operationally. Need to reprocess past C-RDRs and create Support Data files. Will assess this need as users request.

PREDECISIONAL DRAFT INFORMATION

7/14/2014

● = On-track
 ● = Potential management action required
 ● = Management attention required



CDR Program Office


OISST Research to Operations Project

Weekly Report – May 30, 2014

1 OISST – Optimum Interpolated Sea Surface Temperature


- Gathering test data for the SAT and dry runs.
- Completed GHRSSST 2.0 output code updates.
- Successfully completed 30 day parallel test.
- Comparing NCDC GTS with NCEP ship/buoy data for use. GCAD is resolving issues but requires new operational code.
- AVHRR data for the 15 day delay product is available from CLASS.
- Running test data and code on Rainband for parallel test.
- GSTWG discussing inputs and production of preliminary OISST.
- Created a SOP for operational OISST.
- Completed refactoring of each component.
- Conducted Technology Assessment Review July 25.

Operations:

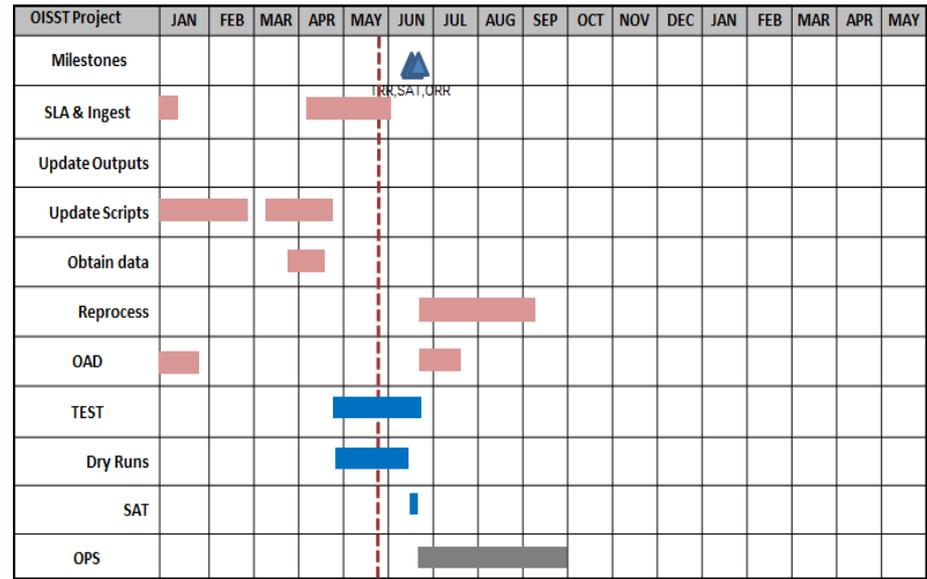

R2O PHASE: ANALYSIS DESIGN DEVELOPMENT INTEGRATION TEST OPERATIONAL

Risk Matrix

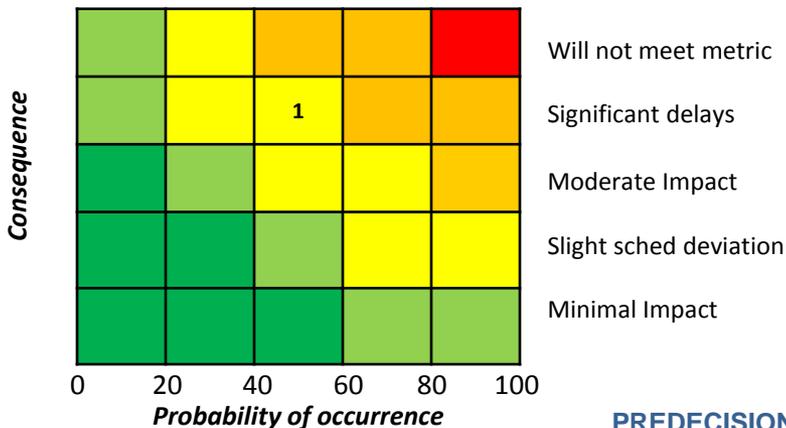

Risk and Mitigation

1 Time to progress through the three tier environment. ITB support is required.

PREDECISIONAL DRAFT INFORMATION






CDR Program Office Operations Monitoring Tool

Weekly Report – May 30, 2014

1 Operations Monitoring Tool development

- Created a Project Plan.
- Need to resolve resource questions to scope project.
- Monitoring of ingest and archive data streams.
- Monitoring of operational processing.

Risk Matrix

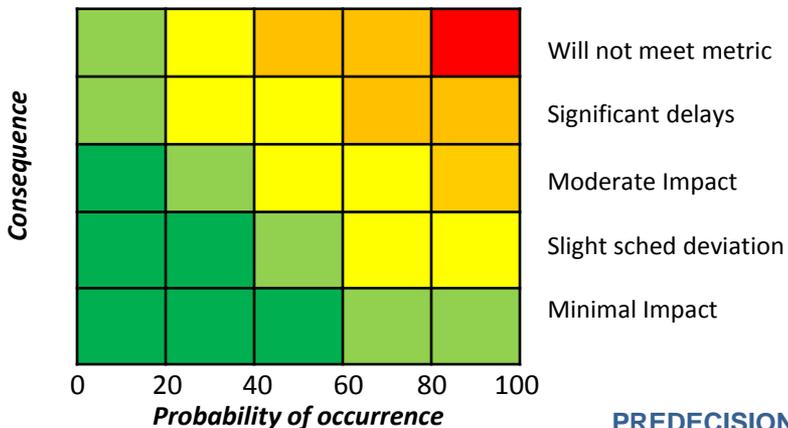

Risk and Mitigation

PREDECISIONAL DRAFT INFORMATION

